PACS — Communication plan

How the team stays aligned: how work is agreed, how it is reviewed, how it is released, and where a decision lives once it is taken.

This is a description of what this repository actually enforces, not a template. Every mechanism named below exists in the project — in `.github/workflows/ci.yml`, in the branch protection on `development`, in `.githooks/pre-commit`, in the CloudFormation under `pipeline/dev/`, or in the comments in the source. Where something is a proposal for when the team grows past one engineer, it says so.

---

1. The current shape of the team, stated honestly


One engineer is building this, as a promotion assessment, and the same person holds the GitHub administrator rights. That matters for two reasons, and both of them have shaped the mechanics:

- **The process is designed so it keeps working when a second person arrives.** Branch protection requires an approving review even though there is nobody else to give one. The rule is not theatre: it is the thing that must already be true on the day the team is two, and a rule introduced later always arrives as an accusation.
- **No gate is trusted just because somebody promised to run it.** `enforce_admins` is off, so the administrator *can* bypass branch protection. The Build stage of the pipeline therefore re-runs the type check and the API unit suite rather than trusting the Actions run that preceded it. A pipeline that trusts a check it did not run is a pipeline that will one day deploy something that does not compile; a minute of CodeBuild buys that away.

Everything below is written for the team this becomes, with the places where one person plays both parts marked.

---

2. The path a change takes

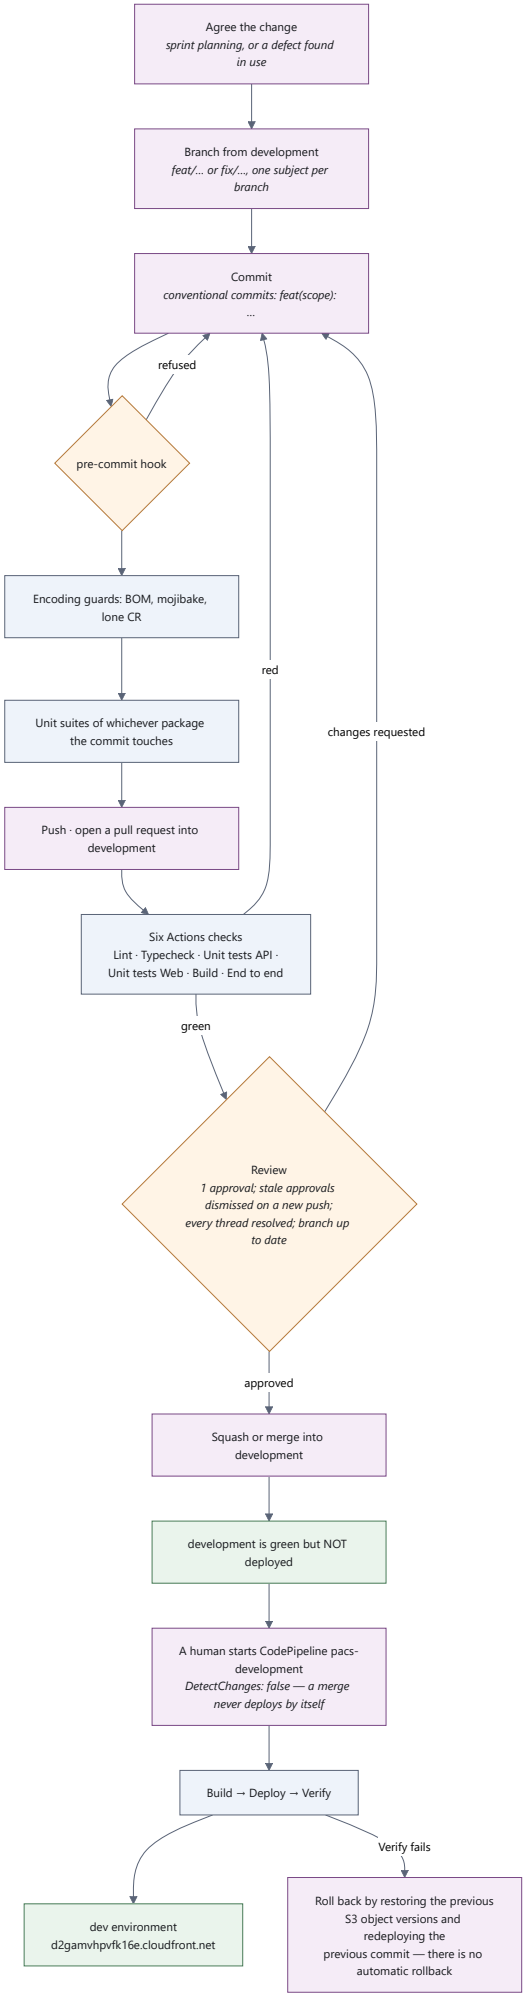
Agree the change
sprint planning, or a defect found in use
Branch from development
feat/... or fix/..., one subject per branch
Commit
conventional commits: feat(scope): ...
refused
pre-commit hook
Encoding guards: BOM, mojibake, lone CR
red
Unit suites of whichever package the commit touches
changes requested
Push · open a pull request into development
Six Actions checks
Lint · Typecheck · Unit tests API · Unit tests Web · Build · End to end
green
Review
1 approval; stale approvals dismissed on a new push; every thread resolved; branch up to date
approved
Squash or merge into development
development is green but NOT deployed
A human starts CodePipeline pacs-development
DetectChanges: false — a merge never deploys by itself
Build → Deploy → Verify
Verify fails
dev environment
d2gamvhpvfk16e.cloudfront.net
Roll back by restoring the previous S3 object versions and redeploying the previous commit — there is no automatic rollback

Three properties of that path are worth naming, because they are what the team actually relies on:

A merge is not a release. `DetectChanges: false` on the pipeline's source action means `development` can be merged into all day without the environment moving. Somebody releases deliberately. The practical value shows up on the day a demonstration is running: nobody has to ask the rest of the team to stop merging.

The gate is on the pull request, not after it. CodePipeline starts after a merge; by then there is nothing to stop. That is exactly why the six checks live in GitHub Actions and why none of them touches AWS — they need no credentials, no OIDC role and no network beyond the registry, which is also what makes them safe to run on a pull request from a fork of a public repository.

The local hook is a courtesy to the reviewer, not a substitute for the checks. It runs the unit suites of whichever package the commit touches, so a commit that edits only the pipeline templates or a document pays nothing. `git commit --no-verify` exists for a deliberate work-in-progress commit, and using it is not a transgression — the pull request will still be told.

---

3. Code review

3.1 What the machine checks, so a human does not have to

Branch protection on `development`, as configured today:

Setting	Value
Required approving reviews	**1**
Stale approvals dismissed on a new push	yes
Required conversation resolution	yes
Required status checks	**Lint · Typecheck · Unit tests API · Unit tests Web · Build · End to end**
Branch must be up to date before merging	yes
Force pushes · branch deletion	both refused
Administrators included	**no** — the one deliberate escape hatch, covered by the pipeline re-running the suites
Required signatures · linear history	not enforced

Plus, before a commit even exists, `.githooks/pre-commit`:

1. **No UTF-8 BOM** in a staged `.json`, `.ts`, `.mjs`, `.js`, `.yml`, `.yaml` or `.md`.
2. **No doubly-encoded UTF-8**: UTF-8 bytes read as Latin-1 and written back as UTF-8, so an em dash arrives as three characters beginning with a circumflexed lower-case a, and a section sign as two beginning with a circumflexed upper-case A. The hook's regular expression lists the exact sequences; this document deliberately does not, because it would then be a file the hook refuses.
3. **No carriage return outside a CRLF pair.**
4. Then the unit suites of the packages the commit touches. `packages/` counts as touching both.

All three encoding guards exist because all three defects actually happened here. A BOM on `package.json` made Vite refuse to parse it with an error that named no file, and cost one red pull request. The mojibake reached `apps/api/package.json`'s description and, unlike a BOM, stays visible in the file for anyone to read. The lone carriage return is the worst of the three: git's `text=auto` detection treats one as a sign of a binary file, so the `eol=lf` in `.gitattributes` stops applying, and four admin pages ended up classified as binary — one of them with a CR sitting where the "r" of "resident" belonged, inside a comment, invisible. The encoding checks run *before* the suites, because a BOM is a one-line fix and waiting out the tests to be told about it is twenty seconds spent learning nothing.

The hook is version-controlled rather than living in `.git/hooks`, and `pnpm install` points git at it through the root `prepare` script. A fresh clone gets it by installing.

3.2 What a human is for

The machine has already established that it compiles, lints, passes 231 API tests and 29 web tests, builds, and survives Playwright. A review that re-checks any of that is wasted. What a reviewer is actually reading for, in rough order of value on this codebase:

1. **Is the rule in the right ring?** Business rules belong in `domain/`, pure and synchronous. The clearest review comment this project has produced is "this is a decision, and it is in `infrastructure/`". The snapshot query is a standing example of the rule: it emits facts — anchors, counts, flags — and never a priority key, because duplicating the key formula in SQL and TypeScript would guarantee drift, and the drift would be invisible until a resident compared their dashboard with the run page.
2. **Does the comment say *why*?** The convention here is heavier than usual and it is deliberate: a comment that restates the code is noise, a comment that records the alternative that was rejected is the only durable place that reasoning lives. If a change makes a non-obvious choice and the diff does not explain it, that is a review comment, and it is the most common one.
3. **Is there a test next to the code?** `*.spec.ts` beside the file it tests. A new domain rule without one is incomplete, not "to be followed up".
4. **Does it widen a boundary?** New route, new role check, new IAM statement, new column on an append-only table, anything that makes an identifier reachable from a path. These get read twice.
5. **Would a resident understand the refusal?** Every blocker in this codebase returns the sentence an administrator is shown, not a boolean. A new one that returns `false` is sending somebody to support.
6. **Is the change one subject?** The seven pull requests merged so far run from 23 to 1,367 lines changed, each with a single subject in its title. A branch that has accumulated two subjects is two pull requests.

3.3 How review is conducted

- **Review on the pull request, in threads, never over a call alone.** A decision reached verbally and merged leaves the next person reading the diff with no explanation. If a call is the fastest way to resolve something, the outcome goes back into the thread before the merge — which is also what "required conversation resolution" is there to make habitual.
- **A comment states the problem, the location and the suggested fix.** Three lines. Review prose costs the author time to parse and the reviewer nothing to omit.
- **Distinguish a blocker from a preference out loud.** "This must change before merge" and "I would have done this differently" are different sentences and should look different. Anything that is a preference and still worth saying is said once and then dropped.

- **The author resolves threads, the reviewer confirms.** The branch cannot merge until every one is resolved, so an unresolved preference is an accidental blocker.
- **An approval is for the commit that was approved.** A new push dismisses it. That is a setting, not a courtesy.
- **While the team is one person**, the review step is self-review against this list, on the pull request page, with the comments written down. Reading one's own diff as a reviewer rather than as an author catches a surprising amount, and it leaves the record that makes the second engineer's first review feel normal rather than ceremonial.

3.4 What gets written where


The change	Where the reasoning goes
Why this code is shaped this way	A comment above it. This is the default and it is the strongest convention in the repository
Why this product rule exists	`apps/web/PRODUCT.md` — users, jobs, the mechanism, the durable constraints
Why this technology, at the scale of the whole system	An ADR in `docs/analisis.html`. ADR-014 lambdalith, ADR-016 no NAT, ADR-017 DynamoDB as cache, and so on
Why this release did what it did	The pull request body and the conventional commit subject
Why the deployed reality differs from the specification	The deviations table in `apps/api/README.md`, and §13 of the technical documentation

The rule behind the table: **a decision is not made until it is written somewhere a stranger would find it.** The place is chosen by who needs it — a reader of this line of code, a reader of this product, or a reader of this architecture.

---

4. Sprint planning

A two-week cadence. The ceremonies below are deliberately few; on a team this size the expensive failure is not under-planning, it is spending a morning agreeing what everyone already knew.



What planning actually decides

The sprint goal is one sentence naming an outcome, not a list of tickets. The ones this project has actually had read like "a run leaves no row at all" and "the Verify stage leaves nothing an administrator can see" — both of which are pull request titles, because the sprint goal and the change that satisfies it should be recognisably the same thing.

Work is sized by risk, not by hours. Three buckets:

- *Known* — the shape is clear, the tests are obvious. Estimate and commit.
- *Known-shaped but unmeasured* — the approach is clear and a number is not, usually because it touches AWS. Timebox it and report what was learned.
- *Unknown* — a spike with a written outcome and no deliverable code expected. The threshold calibration described in `MODULO-PLACAS.md` §8 is one of these: a week of shadow operation producing numbers, not a feature.

Anything that touches the deployed environment is planned with its rollback. There is no automatic rollback in the pipeline. The S3 bucket is versioned with a 30-day noncurrent expiry *specifically* so a bad frontend deploy can be undone by restoring the previous objects; a bad backend deploy is undone by redeploying the previous commit. A plan that does not say which of those applies is not finished.

Migrations are planned as their own step, with a named person and a named machine. They are not in the pipeline and cannot be: CodeBuild sits outside the VPC and its address changes every run, so the security group on `hotel-db` cannot admit it. A sprint containing a migration has an explicit item that says who runs `migrate:up`, from where, and *before which deploy*. This is the single most likely way for this project to break its own environment, and it is the reason the item exists.

Carry-over is discussed, not hidden. A branch open across a sprint boundary is reported at planning with what it is waiting on. The branch protection requires an up-to-date branch before merge, so a long-lived branch becomes somebody's rebasing problem, and the cost grows quietly.

The backlog


Items live in Jira. An item is ready for a sprint when it has: the outcome in a sentence, the rule or the screen it touches, and the observable that says it is done. "Observable" means a test, a command, or a thing a person can see on the dev environment — the same standard the Verify stage holds itself to.

Three standing sources of backlog items, each of which has already produced real work:

1. **The gap list** — §13 of the technical documentation, and the "Not built yet" section of `apps/api/README.md`.
2. **Defects found in use.** Two periods ACTIVE at once with the same bay assigned to two residents was found by looking at the dev environment, not by a test. It became `drawBlocker` and `POST /cycles/{id}/close` in a single sprint item.
3. **The comments.** Several comments in the source name the follow-up explicitly — the migration Lambda inside the VPC, `verify-full` TLS to the database, the crop writer, wiring Transloco. These are backlog items that have already been written; they only need lifting.

---

5. How decisions get made

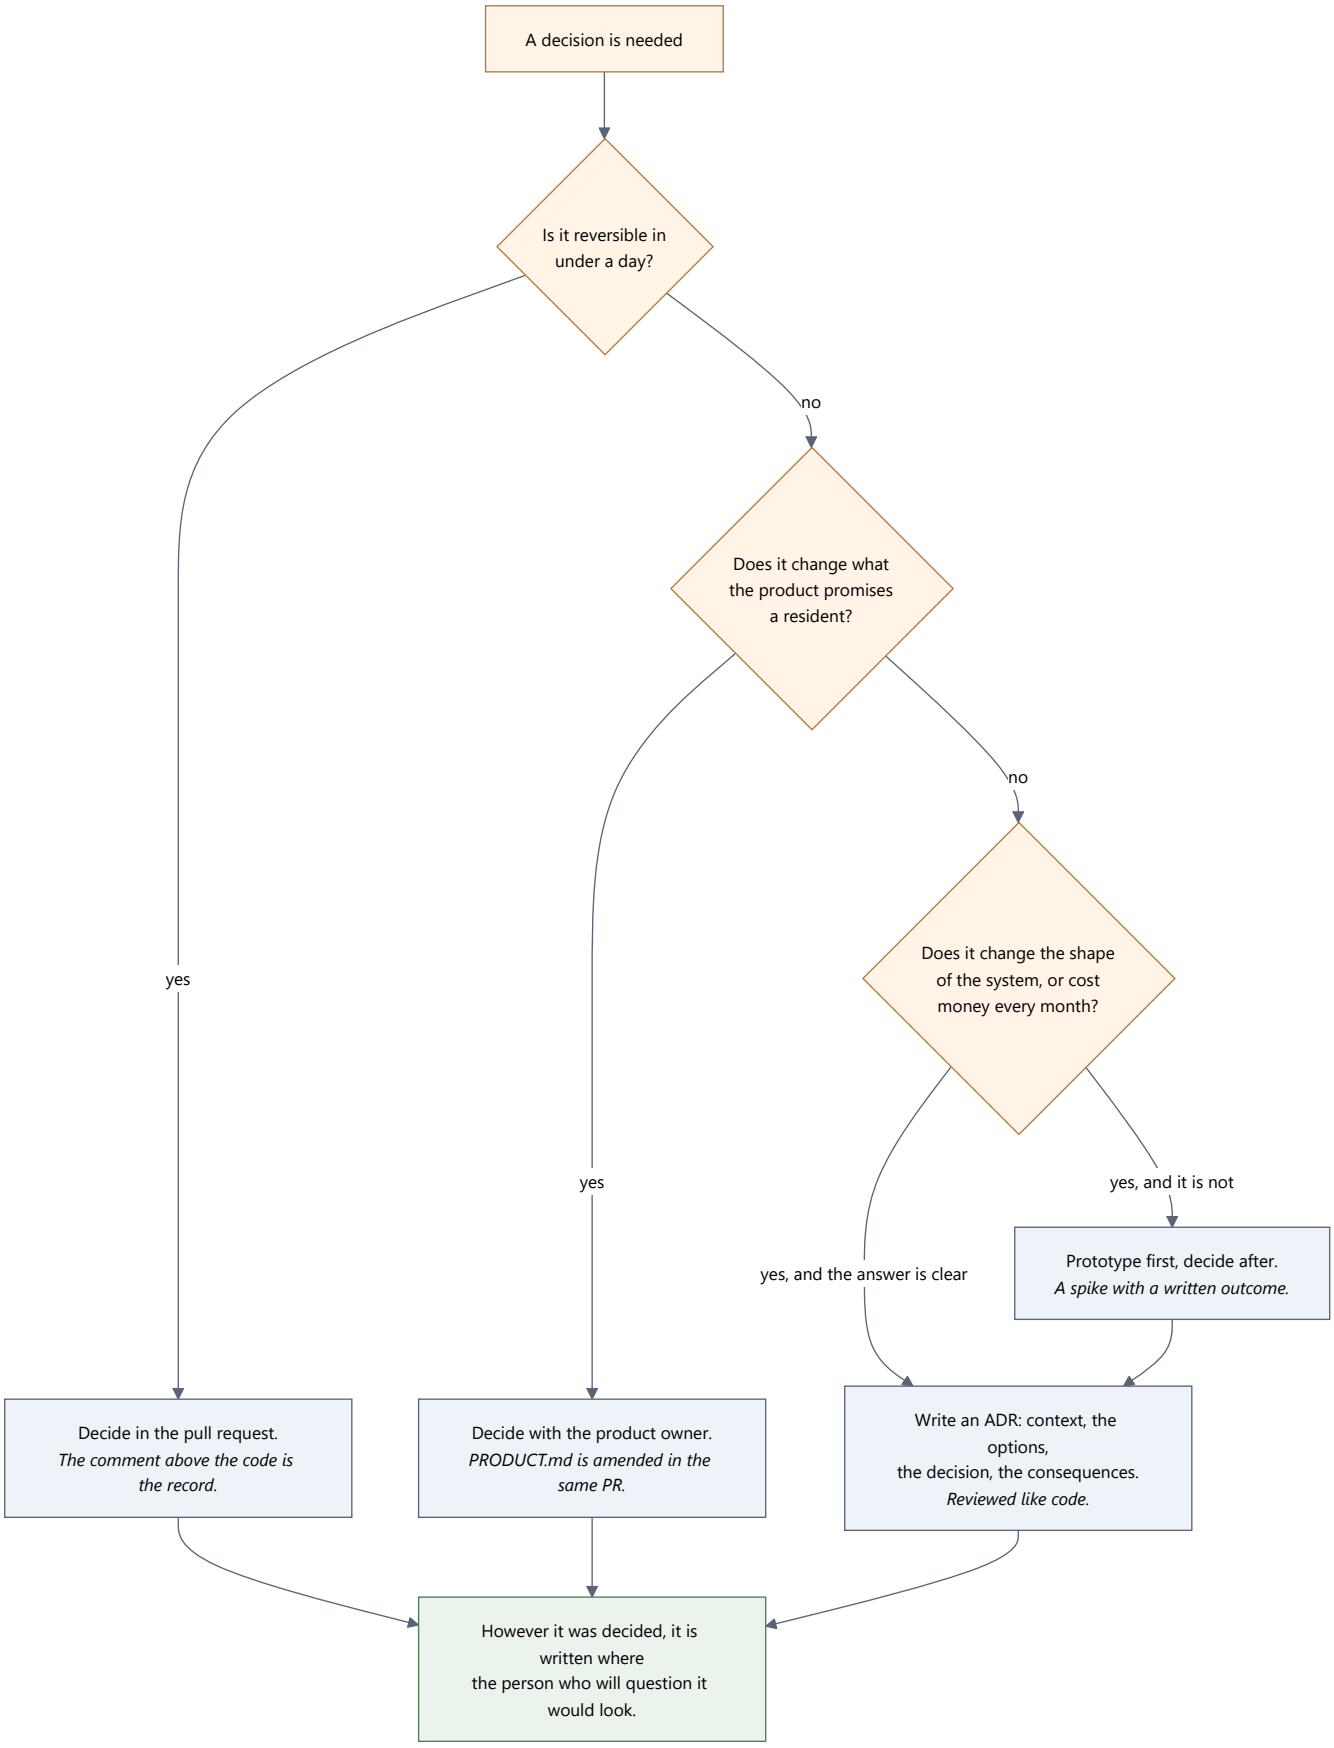

The rules behind that diagram

Reversibility sets the ceremony. Most decisions are cheap to undo and should be made by whoever is holding the keyboard, with a comment explaining the alternative they rejected. Spending a meeting on a one-day decision costs more than being wrong about it.

An expensive decision gets written down before it is taken, not after. An ADR here has four parts and no more: what the situation is, what the options were, what was chosen, and what that costs. The consequences section is the one that earns its keep — ADR-016's "no NAT gateway" consequence is "an in-VPC function reaches exactly RDS and DynamoDB", and every strange thing about this architecture descends from that one line. An ADR that lists only benefits has not been written yet.

A constraint the account imposes is recorded as a constraint, never as a preference. The deviations table in `apps/api/README.md` has a "Why" column for exactly this, and some of its rows are not flattering: `us-east-2` because an SCP denies everything else; CodePipeline because an SCP makes OIDC impossible; no reserved concurrency because the account quota is 10. A reader who cannot tell a forced constraint from a design choice will undo the constraint and break the system.

Disagreement is resolved by making it concrete. Two defensible options and no evidence is a spike, not a debate. The engine choice for plate recognition is the model: three options were costed per read, the expensive one was chosen for reasons that were written down (no second language in the monorepo, no AGPL obligation, no 8-to-15-second cold start failing the first car of the day), and the whole thing was put behind a port so that being wrong costs one class in `infrastructure/` and one line in `src/main`. **Designing so the decision can be revisited is usually cheaper than getting it right first time.**

A decision stays open until somebody can state what would change it. `PRODUCT.md` has an "Open" section carrying exactly this — whether accessible-bay handling stays in the product, and what reactivation should do for a resident who leaves and returns. Writing a question down as open is a decision; leaving it undiscussed is not.

Decisions are revisited when the evidence arrives, and the revision replaces the original. The fairness model is the example that matters: `docs/analisis.html` sections 12 and 13 describe a probabilistic weighted lottery that was superseded by the deterministic rules A–F. The lesson the team took from it is in this plan: when a decision is replaced, the superseded text must be marked as superseded where it lives, or the next reader implements it.

---

6. Communicating outside the team

Audience	What they need	How it reaches them
The building administrator	What changed on the screens they work in, and anything that changes how a draw behaves	Release notes written from the merged pull request titles, sent when the pipeline's Verify stage passes — never when the merge happens, because a merge is not a release here
A resident	Nothing, routinely. A change to the allocation rules is the exception	The fairness explanation the product already generates (`GET /runs/{id}/explanation`), plus a notice from the administrator. A policy change is a new `allocation_config` version with `changed_by` and `changed_at`, so the record of what changed and when exists whether or not anybody writes a notice
A resident contesting a result	The arithmetic, not a policy	`GET /runs/{id}` gives the seed and its commitment; `/explanation` gives the paragraph; the raffle token is `sha256(seed:runId:residentId)` and they can recompute it themselves
Evaluators and reviewers of this project	Why, far more than what	This documentation set, the ADRs, and the comments — which is why the comment convention is treated as a deliverable rather than as a nicety

7. What is deliberately not in place yet

Named so that nobody mistakes an absence for an oversight.

- **No `CODEOWNERS` file and no pull request template.** Both are one-person-team noise today and both should land on the day the team is two: `CODEOWNERS` so the right person is requested automatically, and a template so "what did you consider and reject" is a field rather than a habit.
- **`enforce_admins` is off.** It should go on when the team is two. Until then, turning it on would mean no change could ever be merged.
- **No scheduled dependency updates.** `pnpm install --frozen-lockfile` everywhere means the lockfile is the contract, which is the right half of the problem; nothing currently proposes raising it.
- **No alerting route off the two CloudWatch alarms.** They exist and they fire into the console; nobody is paged. A dev environment does not warrant it, and the day one of these stacks carries a real building, it does.
- **No status page or incident process.** The same judgement, for the same reason.
