PACS — Communication plan

How the team stays aligned: how work is agreed, how it is reviewed, how it is released, and where a decision lives once it is taken.

This is a description of what this repository actually enforces, not a template. Every mechanism named below exists in the project — in `.github/workflows/ci.yml`, in the branch protection on `development`, in `.githooks/pre-commit`, in the CloudFormation under `pipeline/dev/`, or in the comments in the source. Where something is a proposal for when the team grows past one engineer, it says so.

---

1. The current shape of the team, stated honestly


One engineer is building this, as a promotion assessment, and the same person holds the GitHub administrator rights. That matters for two reasons, and both of them have shaped the mechanics:

- **The process is designed so it keeps working when a second person arrives.** Branch protection requires an approving review even though there is nobody else to give one. The rule is not theatre: it is the thing that must already be true on the day the team is two, and a rule introduced later always arrives as an accusation.
- **No gate is trusted just because somebody promised to run it.** `enforce_admins` is off, so the administrator *can* bypass branch protection. The Build stage of the pipeline therefore re-runs the type check and the API unit suite rather than trusting the Actions run that preceded it. A pipeline that trusts a check it did not run is a pipeline that will one day deploy something that does not compile; a minute of CodeBuild buys that away.

Everything below is written for the team this becomes, with the places where one person plays both parts marked.

---

2. The path a change takes

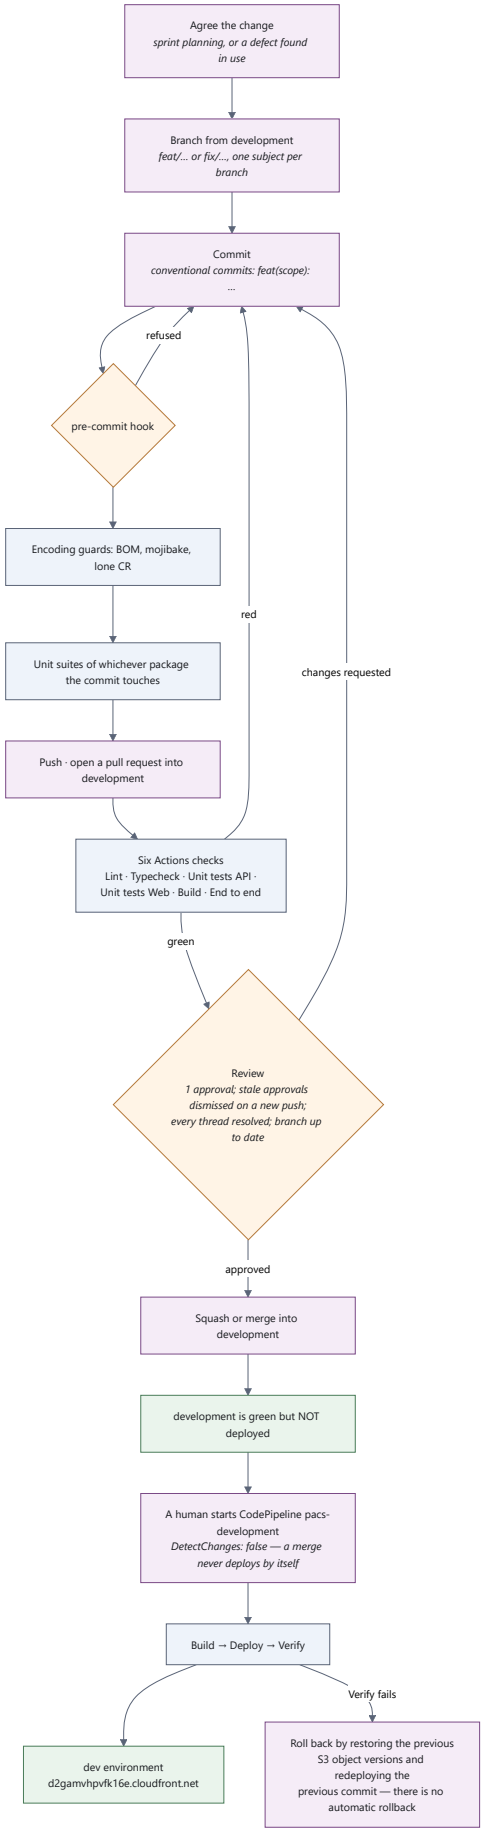

Three properties of that path are worth naming, because they are what the team actually relies on:

A merge is not a release. `DetectChanges: false` on the pipeline's source action means `development` can be merged into all day without the environment moving. Somebody releases deliberately. The practical value shows up on the day a demonstration is running: nobody has to ask the rest of the team to stop merging.

The gate is on the pull request, not after it. CodePipeline starts after a merge; by then there is nothing to stop. That is exactly why the six checks live in GitHub Actions and why none of them touches AWS — they need no credentials, no OIDC role and no network beyond the registry, which is also what makes them safe to run on a pull request from a fork of a public repository.

The local hook is a courtesy to the reviewer, not a substitute for the checks. It runs the unit suites of whichever package the commit touches, so a commit that edits only the pipeline templates or a document pays nothing. `git commit --no-verify` exists for a deliberate work-in-progress commit, and using it is not a transgression — the pull request will still be told.

---

3. Code review

3.1 What the machine checks, so a human does not have to

Branch protection on `development`, as configured today:

Setting	Value
Required approving reviews	**1**
Stale approvals dismissed on a new push	yes
Required conversation resolution	yes
Required status checks	**Lint · Typecheck · Unit tests API · Unit tests Web · Build · End to end**
Branch must be up to date before merging	yes
Force pushes · branch deletion	both refused
Administrators included	**no** — the one deliberate escape hatch, covered by the pipeline re-running the suites
Required signatures · linear history	not enforced

Plus, before a commit even exists, `.githooks/pre-commit`:

1. **No UTF-8 BOM** in a staged `.json`, `.ts`, `.mjs`, `.js`, `.yml`, `.yaml` or `.md`.
2. **No doubly-encoded UTF-8**: UTF-8 bytes read as Latin-1 and written back as UTF-8, so an em dash arrives as three characters beginning with a circumflexed lower-case a, and a section sign as two beginning with a circumflexed upper-case A. The hook's regular expression lists the exact sequences; this document deliberately does not, because it would then be a file the hook refuses.
3. **No carriage return outside a CRLF pair.**
4. Then the unit suites of the packages the commit touches. `packages/` counts as touching both.

All three encoding guards exist because all three defects actually happened here. A BOM on `package.json` made Vite refuse to parse it with an error that named no file, and cost one red pull request. The mojibake reached `apps/api/package.json`'s description and, unlike a BOM, stays visible in the file for anyone to read. The lone carriage return is the worst of the three: git's `text=auto` detection treats one as a sign of a binary file, so the `eol=lf` in `.gitattributes` stops applying, and four admin pages ended up classified as binary — one of them with a CR sitting where the "r" of "resident" belonged, inside a comment, invisible. The encoding checks run *before* the suites, because a BOM is a one-line fix and waiting out the tests to be told about it is twenty seconds spent learning nothing.

The hook is version-controlled rather than living in `.git/hooks`, and `pnpm install` points git at it through the root `prepare` script. A fresh clone gets it by installing.

3.2 What a human is for

The machine has already established that it compiles, lints, passes 267 API tests and 69 web tests, builds, and survives Playwright. A review that re-checks any of that is wasted. What a reviewer is actually reading for, in rough order of value on this codebase:

1. **Is the rule in the right ring?** Business rules belong in `domain/`, pure and synchronous. The clearest review comment this project has produced is "this is a decision, and it is in `infrastructure/`". The snapshot query is a standing example of the rule: it emits facts — anchors, counts, flags — and never a priority key, because duplicating the key formula in SQL and TypeScript would guarantee drift, and the drift would be invisible until a resident compared their dashboard with the run page.
2. **Does the comment say *why*?** The convention here is heavier than usual and it is deliberate: a comment that restates the code is noise, a comment that records the alternative that was rejected is the only durable place that reasoning lives. If a change makes a non-obvious choice and the diff does not explain it, that is a review comment, and it is the most common one.
3. **Is there a test next to the code?** `*.spec.ts` beside the file it tests. A new domain rule without one is incomplete, not "to be followed up".
4. **Does it widen a boundary?** New route, new role check, new IAM statement, new column on an append-only table, anything that makes an identifier reachable from a path. These get read twice.
5. **Would a resident understand the refusal?** Every blocker in this codebase returns the sentence an administrator is shown, not a boolean. A new one that returns `false` is sending somebody to support.
6. **Is the change one subject?** Twenty-two pull requests have merged. Twelve of the last thirteen are under 400 lines changed, most under 100, each with one subject in its title — a defect found in use, fixed and released the same day. The exception proves the rule: #10 is 9,105 lines, its title is a branch name ("Fix/smoke asserts the draw rule") and it carried a menu reorder, a new domain rule and a smoke fix together. It was the hardest to review and the hardest to describe afterwards. A branch that has accumulated two subjects is two pull requests.

3.3 How review is conducted

- **Review on the pull request, in threads, never over a call alone.** A decision reached verbally and merged leaves the next person reading the diff with no explanation. If a call is the fastest way to resolve something, the outcome goes back into the thread before the merge — which is also what "required conversation resolution" is there to make habitual.
- **A comment states the problem, the location and the suggested fix.** Three lines. Review prose costs the author time to parse and the reviewer nothing to omit.

- **Distinguish a blocker from a preference out loud.** "This must change before merge" and "I would have done this differently" are different sentences and should look different. Anything that is a preference and still worth saying is said once and then dropped.
- **The author resolves threads, the reviewer confirms.** The branch cannot merge until every one is resolved, so an unresolved preference is an accidental blocker.
- **An approval is for the commit that was approved.** A new push dismisses it. That is a setting, not a courtesy.
- **While the team is one person**, the review step is self-review against this list, on the pull request page, with the comments written down. Reading one's own diff as a reviewer rather than as an author catches a surprising amount, and it leaves the record that makes the second engineer's first review feel normal rather than ceremonial.

3.4 What gets written where


The change	Where the reasoning goes
Why this code is shaped this way	A comment above it. This is the default and it is the strongest convention in the repository
Why this product rule exists	`apps/web/PRODUCT.md` — users, jobs, the mechanism, the durable constraints
Why this technology, at the scale of the whole system	An ADR in `docs/analisis.html`. ADR-014 lambdalith, ADR-016 no NAT, ADR-017 DynamoDB as cache, and so on
Why this release did what it did	The pull request body and the conventional commit subject
Why the deployed reality differs from the specification	The deviations table in the root `README.md`, and §13 of the technical documentation

The rule behind the table: **a decision is not made until it is written somewhere a stranger would find it.** The place is chosen by who needs it — a reader of this line of code, a reader of this product, or a reader of this architecture.

---

4. Sprint planning

A two-week cadence. The ceremonies below are deliberately few; on a team this size the expensive failure is not under-planning, it is spending a morning agreeing what everyone already knew.



What planning actually decides

The sprint goal is one sentence naming an outcome, not a list of tickets. The ones this project has actually had read like "a run leaves no row at all" and "the Verify stage leaves nothing an administrator can see" — both of which are pull request titles, because the sprint goal and the change that satisfies it should be recognisably the same thing.

Work is sized by risk, not by hours. Three buckets:

- *Known* — the shape is clear, the tests are obvious. Estimate and commit.
- *Known-shaped but unmeasured* — the approach is clear and a number is not, usually because it touches AWS. Timebox it and report what was learned.
- *Unknown* — a spike with a written outcome and no deliverable code expected. The threshold calibration described in `MODULO-PLACAS.md` §8 is one of these: a week of shadow operation producing numbers, not a feature.

Anything that touches the deployed environment is planned with its rollback. There is no automatic rollback in the pipeline. The S3 bucket is versioned with a 30-day noncurrent expiry *specifically* so a bad frontend deploy can be undone by restoring the previous objects; a bad backend deploy is undone by redeploying the previous commit. A plan that does not say which of those applies is not finished.

Migrations are planned as their own step, with a named person and a named machine. They are not in the pipeline and cannot be: CodeBuild sits outside the VPC and its address changes every run, so the security group on `hotel-db` cannot admit it. A sprint containing a migration has an explicit item that says who runs `migrate:up`, from where, and *before which deploy*. This is the single most likely way for this project to break its own environment, and it is the reason the item exists.

Carry-over is discussed, not hidden. A branch open across a sprint boundary is reported at planning with what it is waiting on. The branch protection requires an up-to-date branch before merge, so a long-lived branch becomes somebody's rebasing problem, and the cost grows quietly.

The backlog


Items live in Jira. An item is ready for a sprint when it has: the outcome in a sentence, the rule or the screen it touches, and the observable that says it is done. "Observable" means a test, a command, or a thing a person can see on the dev environment — the same standard the Verify stage holds itself to.

Three standing sources of backlog items, each of which has already produced real work:

1. **The gap list** — §13 of the technical documentation, and the "Not built yet" section of the root `README.md`.
2. **Defects found in use.** Two periods ACTIVE at once with the same bay assigned to two residents was found by looking at the dev environment, not by a test. It became `drawBlocker` and `POST /cycles/{id}/close` in a single sprint item.
3. **The comments.** Several comments in the source name the follow-up explicitly — the migration Lambda inside the VPC, `verify-full` TLS to the database, the crop writer, wiring Transloco. These are backlog items that have already been written; they only need lifting.

---

5. How decisions get made

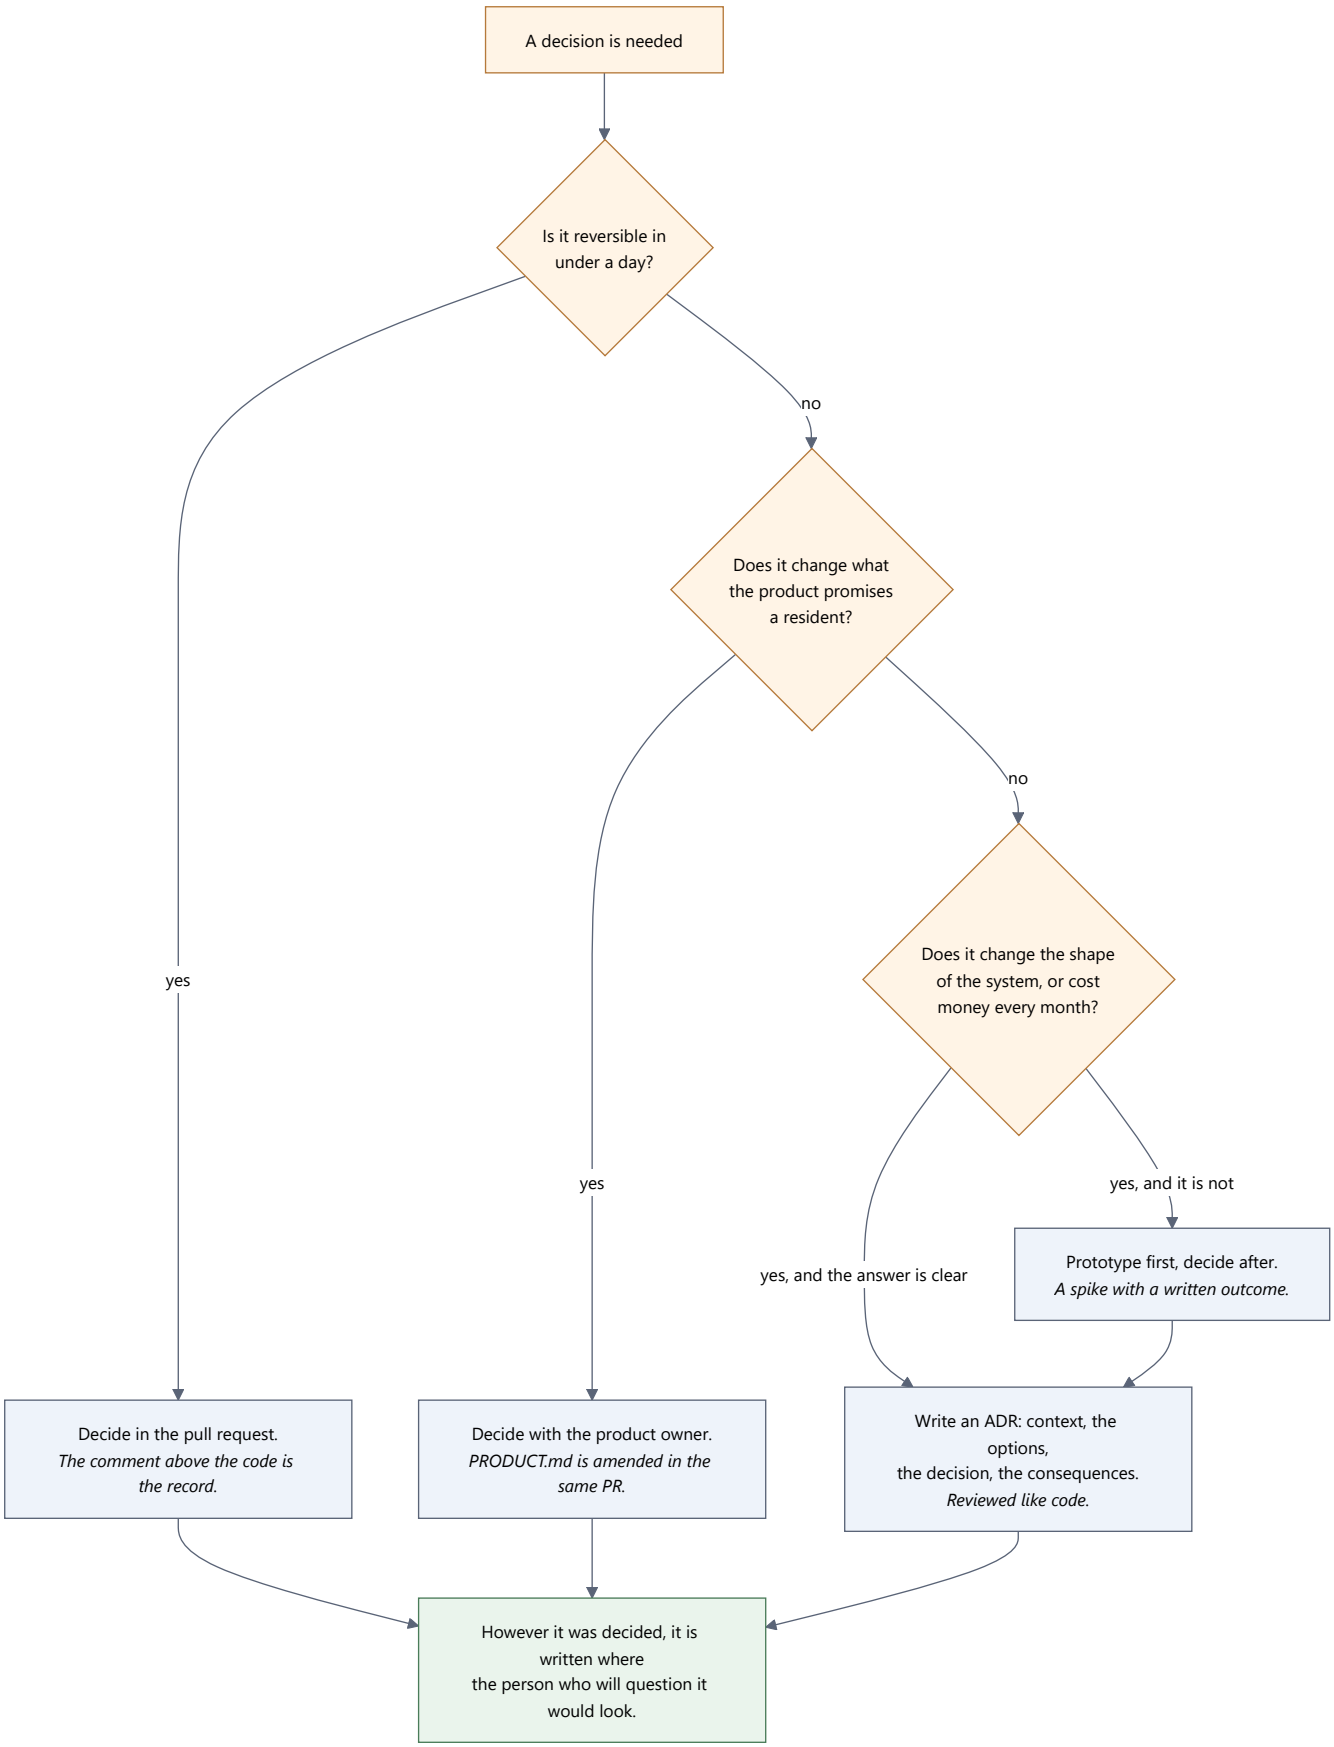

The rules behind that diagram

Reversibility sets the ceremony. Most decisions are cheap to undo and should be made by whoever is holding the keyboard, with a comment explaining the alternative they rejected. Spending a meeting on a one-day decision costs more than being wrong about it.

An expensive decision gets written down before it is taken, not after. An ADR here has four parts and no more: what the situation is, what the options were, what was chosen, and what that costs. The consequences section is the one that earns its keep — ADR-016's "no NAT gateway" consequence is "an in-VPC function reaches exactly RDS and DynamoDB", and every strange thing about this architecture descends from that one line. An ADR that lists only benefits has not been written yet.

A constraint the account imposes is recorded as a constraint, never as a preference. The deviations table in the root `README.md` has a "Why" column for exactly this, and some of its rows are not flattering: `us-east-2` because an SCP denies everything else; CodePipeline because an SCP makes OIDC impossible; no reserved concurrency because the account quota is 10. A reader who cannot tell a forced constraint from a design choice will undo the constraint and break the system.

Disagreement is resolved by making it concrete. Two defensible options and no evidence is a spike, not a debate. The engine choice for plate recognition is the model: three options were costed per read, the expensive one was chosen for reasons that were written down (no second language in the monorepo, no AGPL obligation, no 8-to-15-second cold start failing the first car of the day), and the whole thing was put behind a port so that being wrong costs one class in `infrastructure/` and one line in `src/main`. **Designing so the decision can be revisited is usually cheaper than getting it right first time.**

A decision stays open until somebody can state what would change it. `PRODUCT.md` has an "Open" section carrying exactly this — whether accessible-bay handling stays in the product, and what reactivation should do for a resident who leaves and returns. Writing a question down as open is a decision; leaving it undiscussed is not.

Decisions are revisited when the evidence arrives, and the revision replaces the original. The fairness model is the example that matters: `docs/analisis.html` sections 12 and 13 describe a probabilistic weighted lottery that was superseded by the deterministic rules A–F, later extended to A–H when the building settled how withdrawing and sitting a period out should count. The lesson the team took from it is in this plan: when a decision is replaced, the superseded text must be marked as superseded where it lives, or the next reader implements it.

---

6. Channels, and what goes in each

Five places, each with one job. The failure this table exists to prevent is a decision that lives only where it was made — a call, a chat thread — and is therefore lost to the next person.

Channel	What belongs there	Expected response	What never goes there
The pull request	Review, the reasoning behind a change, anything decided about this diff	Same working day for a first review; the author answers every thread	A decision reached elsewhere and not written back
Jira (`PACS` project)	The backlog: outcome, the rule or screen it touches, the observable that says it is done. Status of work in flight	Updated when the state changes, not at the end of the sprint	Design discussion — link the pull request or the ADR instead
Team chat	Blockers, "I am about to release", "I am demonstrating on dev until 15:00", quick questions	Within the hour during working time	Anything someone will need to find in a month. If it matters, it moves to the PR, Jira or a document, and the chat links it
The written daily	Three lines in the team channel: what moved, what is next, what is blocked	Read by everyone before noon	Status theatre. A day with nothing to report says so in one line
The repository's documents	Product rules (`PRODUCT.md`), architecture (ADRs in `docs/analisis.html`), this set	Changed in the same pull request as the behaviour they describe	Plans that are not yet decisions


Two announcements are **mandatory** in the team channel, because each one changes the environment under somebody else:

- **Before a release** — "starting `pacs-development` at commit `abc1234`: #21, #22" — and its outcome when Verify finishes.
- **Before anything destructive on a shared environment** — a migration, `reset-periods`, `keep-only-users`, a hand-edit in the database. Whoever is demonstrating loses their data too, and finding that out mid-demo is the worst way to.

---

7. A worked example: an incident, from report to release

What the plan looks like when it is used. On 2026-10-14 a person reported, in chat, that a resident they had just created never received the invitation email and could not sign in.

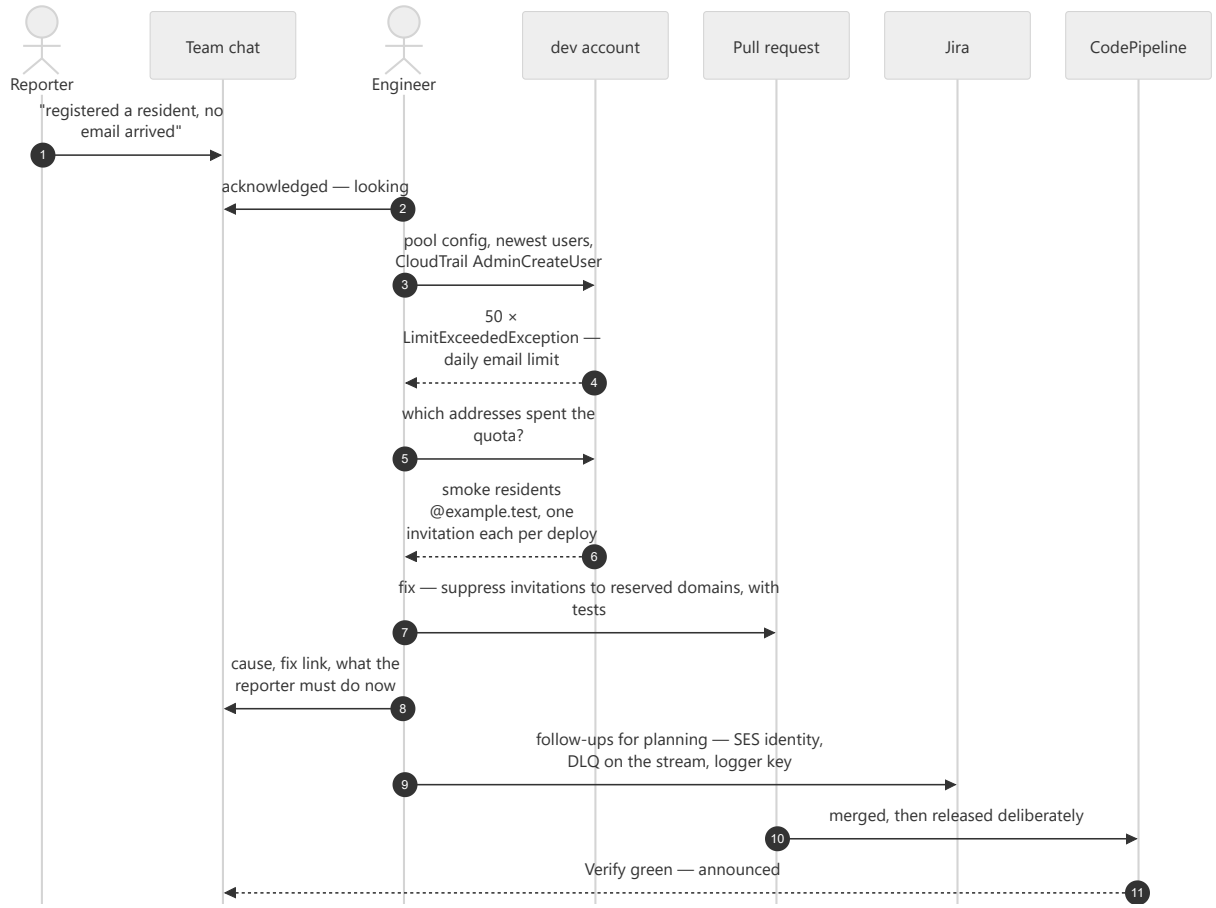

What each step demonstrates, and why it is done that way:

1. **Acknowledge first, diagnose second.** A one-line "looking" stops three people investigating the same thing.
2. **Evidence before theory.** The obvious guesses — spam folder, a typo in the address — were not tested; the account was asked. CloudTrail named the error in one query.
3. **The cause is stated in the pull request, not only in chat.** PR #22's body quotes the error, names the quota and explains why the smoke suites spent it. A reader in six months finds it from `git blame` on the line it changed.
4. **The fix is the smallest one that removes the cause.** Not "configure SES", which needs a verified identity and production access; that is a backlog item with its reason.
5. **The reporter is told what to do now**, in their language, separately from the fix: the affected resident must be provisioned again once the quota resets, because the failed event was dropped.
6. **Every gap found on the way becomes a backlog item, not a footnote.** Three were found: the quota itself, the missing DLQ, and a log line that drops the error text. They are written in §13 of the technical documentation, each with its reason, ready to be lifted into the backlog at the next planning.
7. **The runbook is updated.** §14.2 of the technical documentation now has the exact command that re-provisions a resident. The second time this happens it takes minutes.

The total elapsed time was under an hour, and nothing about it needed a meeting.

8. Communicating outside the team

Audience	What they need	How it reaches them
The building administrator	What changed on the screens they work in, and anything that changes how a draw behaves	Release notes written from the merged pull request titles, sent when the pipeline's Verify stage passes — never when the merge happens, because a merge is not a release here
A resident	Nothing, routinely. A change to the allocation rules is the exception	The fairness explanation the product already generates (`GET /runs/{id}/explanation`), plus a notice from the administrator. A policy change is a new `allocation_config` version with `changed_by` and `changed_at`, so the record of what changed and when exists whether or not anybody writes a notice
A resident contesting a result	The arithmetic, not a policy	`GET /runs/{id}` gives the seed and its commitment; `/explanation` gives the paragraph; the raffle token is `sha256(seed:runId:residentId)` and they can recompute it themselves
Evaluators and reviewers of this project	Why, far more than what	This documentation set, the ADRs, and the comments — which is why the comment convention is treated as a deliverable rather than as a nicety

9. What is deliberately not in place yet

Named so that nobody mistakes an absence for an oversight.

- **No `CODEOWNERS` file.** One-person-team noise today; it lands on the day the team is two, so the right person is requested automatically. The pull request template is already in place (`.github/pull_request_template.md`), so "what did you consider and reject" is a field rather than a habit.
- **`enforce_admins` is off.** It should go on when the team is two. Until then, turning it on would mean no change could ever be merged.
- **No scheduled dependency updates.** `pnpm install --frozen-lockfile` everywhere means the lockfile is the contract, which is the right half of the problem; nothing currently proposes raising it.
- **No alerting route off the two CloudWatch alarms.** They exist and they fire into the console; nobody is paged. A dev environment does not warrant it, and the day one of these stacks carries a real building, it does.
- **No status page or incident process.** The same judgement, for the same reason.
